ID	Task Mode	Task Name	Duration	Start	Finish
1		**WP1. Simulations and Analysis**	**35.55 mons**	**Fri 01/05/20**	**Mon 01/05/23**
2		Atom. Beamline. Simul.	21.82 mons	Fri 01/05/20	Thu 03/03/22
3		CRES Model	21 mons	Fri 01/05/20	Mon 07/02/22
4		M1.1	0 mons	Thu 01/10/20	Thu 01/10/20
5		Trap Simul.	21 mons	Mon 02/11/20	Tue 09/08/22
6		M1.2	0 mons	Mon 11/04/22	Mon 11/04/22
7		M1.3	0 mons	Fri 25/03/22	Fri 25/03/22
8		CRES Analys. And Sensitiv.	20 mons	Tue 08/06/21	Mon 13/02/23
9		M1.4	0 mons	Mon 10/10/22	Mon 10/10/22
10		M1.5	0 mons	Mon 06/03/23	Mon 06/03/23
11					
12		**WP2. Atomic Beam Source and Magnetic Trapping**	**35.55 mons**	**Fri 01/05/20**	**Mon 01/05/23**
13		D-beam construction	9 mons	Mon 04/05/20	Wed 03/02/21
14		M2.1	0 mons	Fri 05/02/21	Fri 05/02/21
15		Zeeman Construction	7 mons	Tue 02/02/21	Fri 03/09/21
16		M2.2	0 mons	Wed 01/09/21	Wed 01/09/21
17		Zeeman Characterisation	4 mons	Mon 06/09/21	Wed 05/01/22
18		M2.3	0 mons	Fri 07/01/22	Fri 07/01/22
19		Trap Construction	18 mons	Mon 11/05/20	Mon 15/11/21
20		M2.4	0 mons	Mon 15/11/21	Mon 15/11/21
21		D-trapping and E-source	7 mons	Mon 15/11/21	Thu 16/06/22
22		M2.5	0 mons	Thu 10/03/22	Thu 10/03/22
23		M2.6	0 mons	Thu 16/06/22	Thu 16/06/22
24		Loading Optimisation	11 mons	Thu 05/05/22	Fri 07/04/23
25		M2.7	0 mons	Mon 10/04/23	Mon 10/04/23
26					
27		**WP3. 3D B-field mapping**	**29.55 mo**	**Mon 02/11/20**	**Fri 28/04/23**
28		D-spectroscopy	6 mons	Mon 02/11/20	Tue 04/05/21
29		M3.1	0 mons	Wed 05/05/21	Wed 05/05/21
30		MW spectroscopy	6 mons	Tue 04/05/21	Wed 03/11/21
31		M3.2	0 mons	Thu 04/11/21	Thu 04/11/21
32		D motion control	6 mons	Mon 01/11/21	Tue 03/05/22
33		M3.3	0 mons	Wed 04/05/22	Wed 04/05/22
34		1D mapping	6 mons	Mon 02/05/22	Tue 01/11/22
35		M3.4	0 mons	Tue 01/11/22	Tue 01/11/22
36		3D mapping	6 mons	Mon 03/10/22	Tue 04/04/23
37		M3.5	0 mons	Mon 10/04/23	Mon 10/04/23
38					
39		**WP4. Cyclotron Radiation Detection**	**35.55 mons**	**Fri 01/05/20**	**Mon 01/05/23**
40		Baseline Receiver	18 mons	Fri 01/05/20	Fri 05/11/21
41		M4.1	0 mons	Fri 05/11/21	Fri 05/11/21
42		SLUG Amplifier	16 mons	Mon 03/05/21	Tue 06/09/22
43		JTWPA amplifier	16 mons	Mon 03/05/21	Tue 06/09/22
44		M4.2	0 mons	Tue 06/09/22	Tue 06/09/22
45		Intergration with trap	6 mons	Mon 25/04/22	Tue 25/10/22
46		M4.3	0 mons	Tue 25/10/22	Tue 25/10/22
47		CRES Detection Runs	7 mons	Mon 12/09/22	Thu 13/04/23
48		M4.4	0 mons	Thu 20/04/23	Thu 20/04/23
49					
50		**WP5. Geonium Atom Detector**	**35.55 mons**	**Fri 01/05/20**	**Mon 01/05/23**
51		Geonium chip in B-field	12 mons	Wed 20/05/20	Mon 24/05/21
52		M5.1	0 mons	Mon 10/05/21	Mon 10/05/21
53		Integration with trap	5 mons	Mon 26/04/21	Fri 24/09/21
54		M5.2	0 mons	Fri 24/09/21	Fri 24/09/21
55		Calibration with MW source	5 mons	Mon 20/09/21	Fri 18/02/22
56		M5.3	0 mons	Fri 18/02/22	Fri 18/02/22
57		CRES Detection Runs with geonium	12 mons	Thu 24/02/22	Tue 28/02/23
58		M5.4	0 mons	Fri 10/03/23	Fri 10/03/23

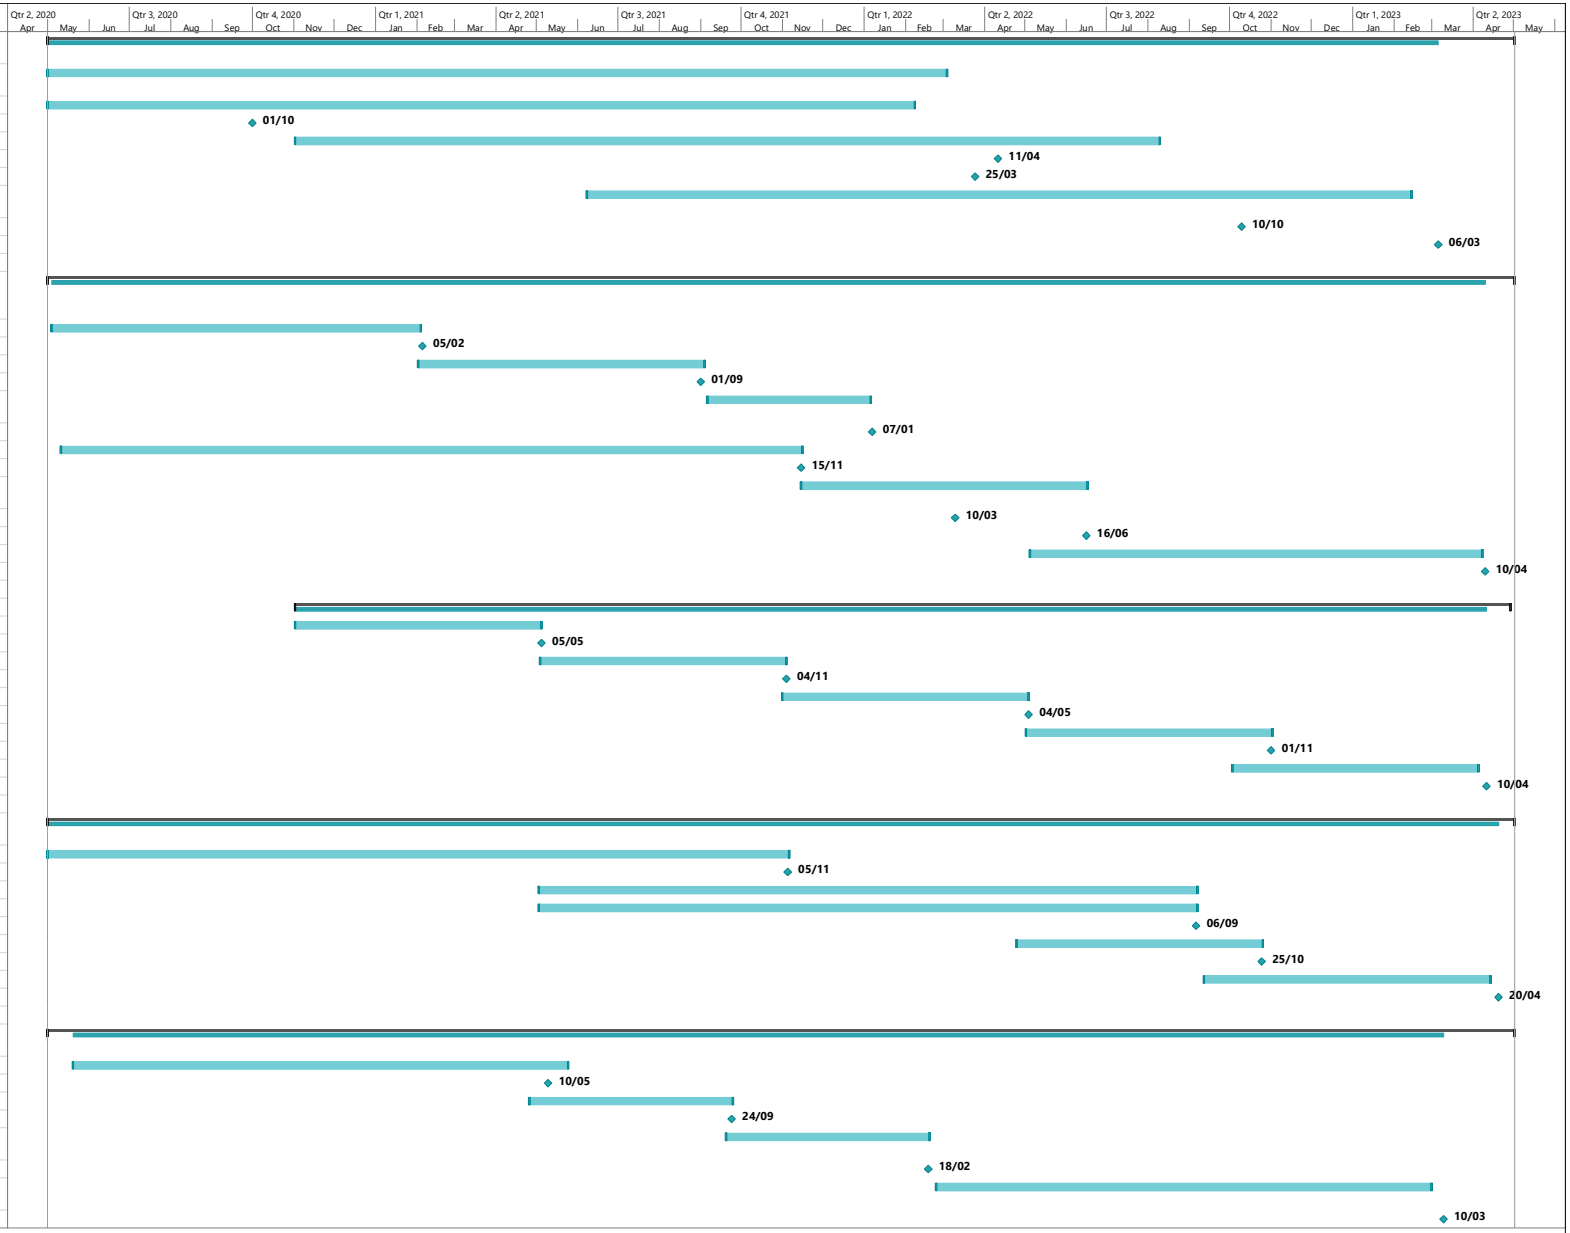

Project: QTNM-GanttChart
Date: Fri 29/11/19

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
